Tree protection plan
Location of trees, categorisation & protection/management proposals

Land west of Bridge, Lower Horsebridge, Hailsham, East Sussex BN27 4DNE

Barrell Plan Ref: 22175-2

Permission is granted to scale from this drawing for Local Authority Planning Approval purposes relating to tree protection measures only. Where applicable this drawing is to be read in conjunction with the arboricultural report. This drawing is the copyright of Barrell Tree Consultancy 2022 ©

This drawing to be reproduced in colour only.

www.barrelltreecare.co.uk

- BS category A — Trees of high quality
- BS category B — Trees of moderate quality
- BS category C — Trees of low quality
- BS category U — Trees unsuitable for retention
- Trees to be removed
- Proposed layout
- Estimated tree positions not included on original land survey and/or adjusted crown spreads
- Protective barrier/fencing
- Construction exclusion zone (CEZ)
- Root protection area (RPA) boundaries for category A and B trees
- Root protection area (RPA) boundaries for category C trees

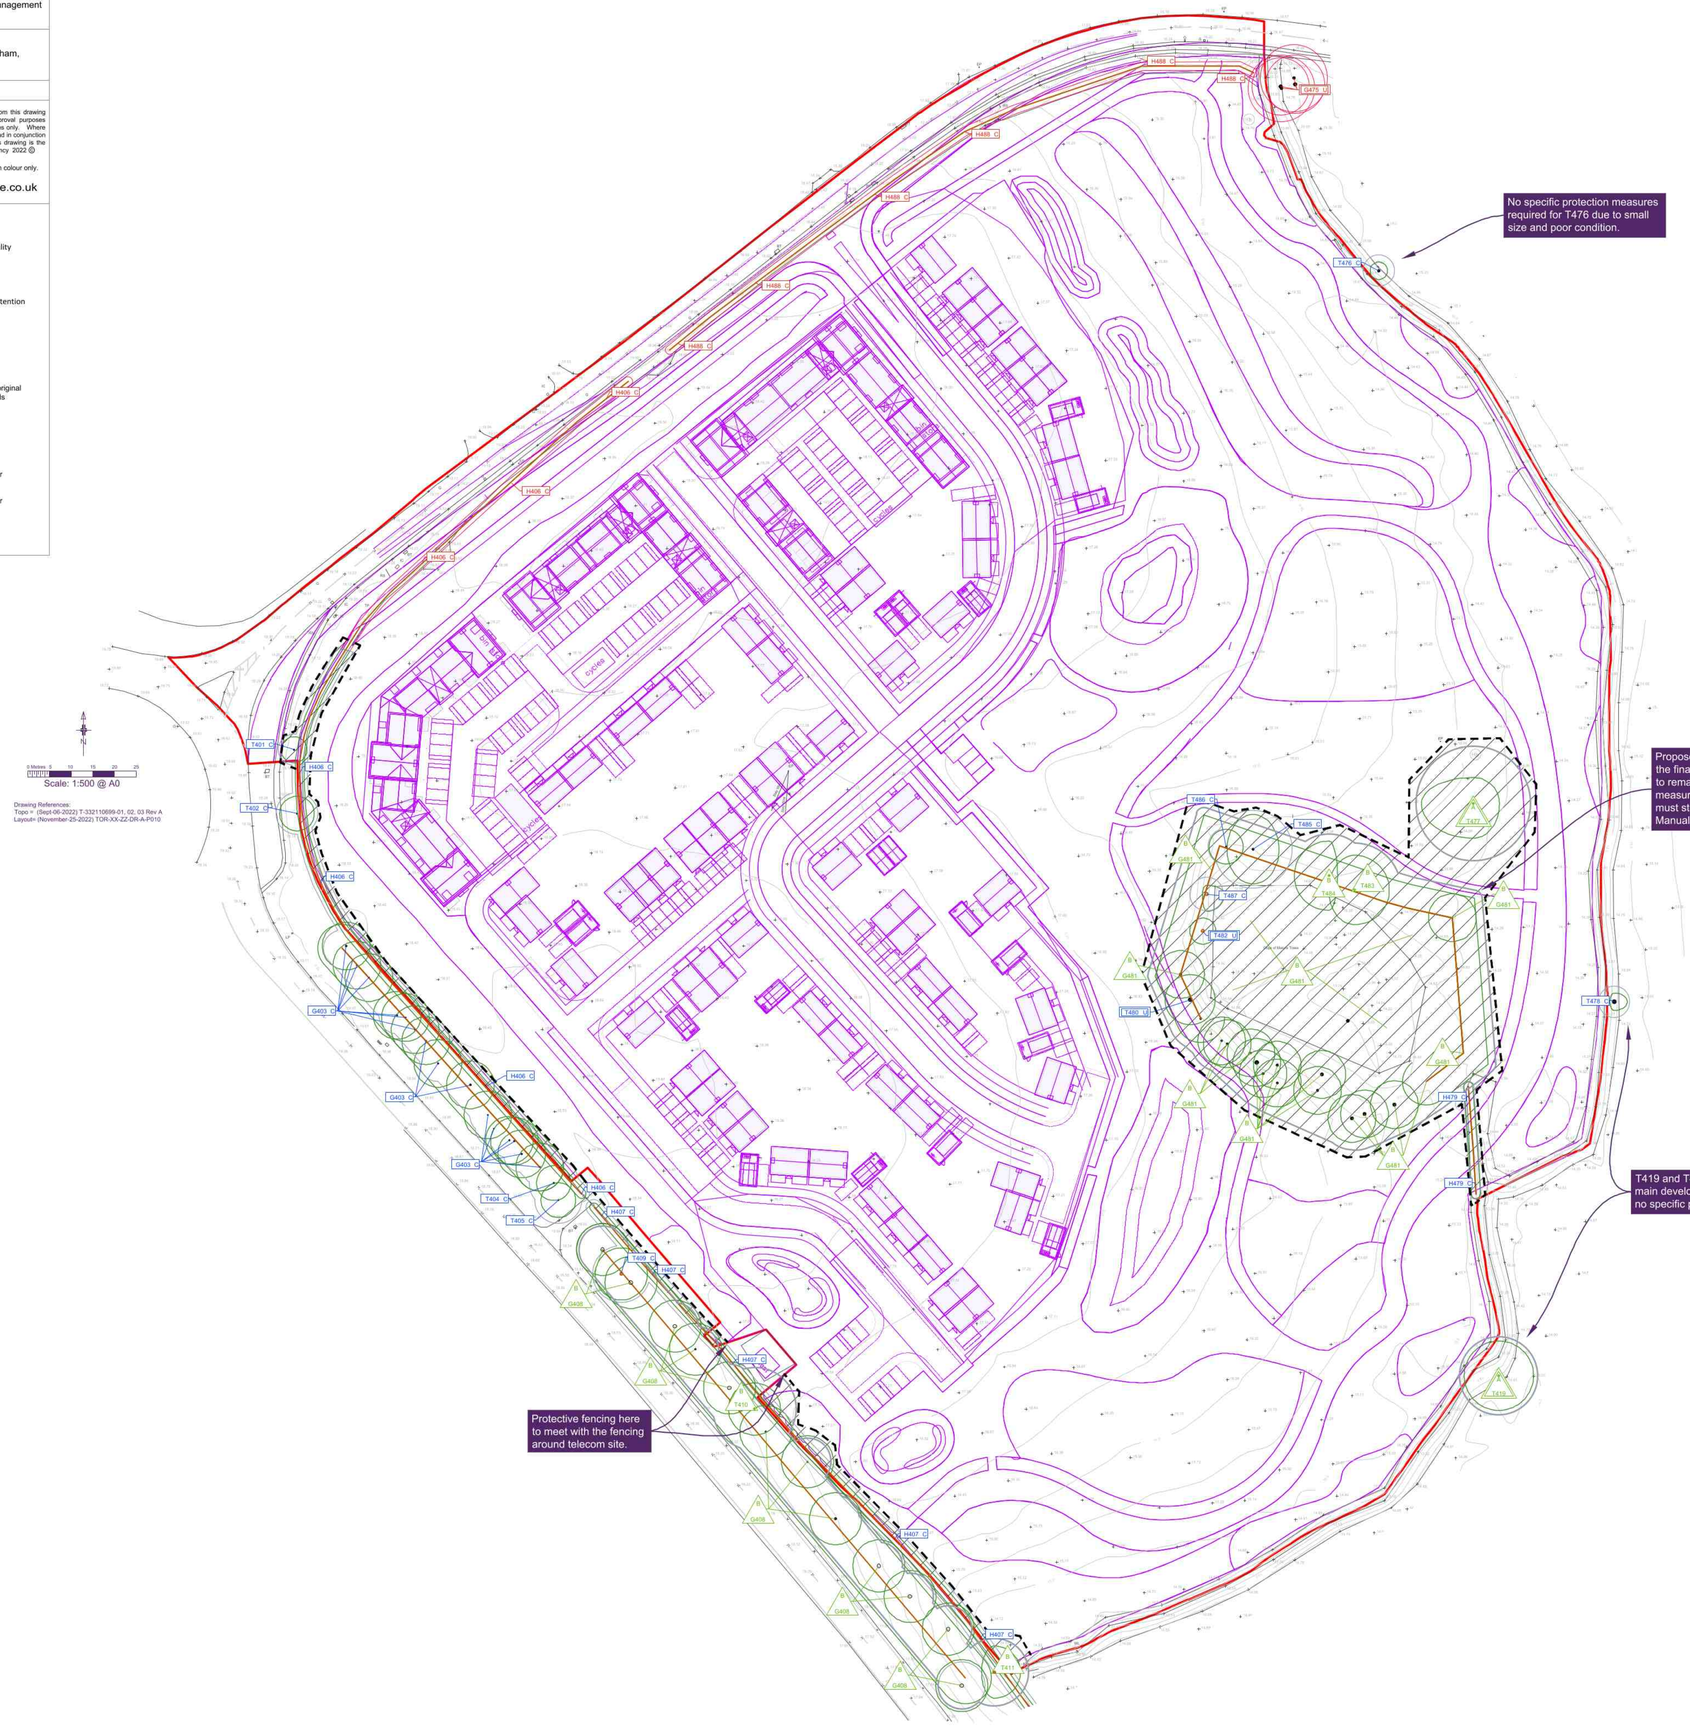

Tree No	Species	Category	RPA Radius	Tree Works
All retained trees & hedges				Carry out safety check and lift over site to 3-4 m as necessary.
T401	Lime	C	3.6	
T402	Lime	C	4.8	
G403	Ash, lime, field maple, oak	C	4.2	
T404	Ash	C	5.7	
T405	Lime	C	5.4	
H406	Hawthorn	C	1.8	Fell (part) for development
H407	Hawthorn	C	1.8	
G408	Ash, lime, field maple, oak	B	5.4	
T409	Ash	C	6.6	
T410	Lime	B	9.6	
T411	Horse chestnut	B	7.8	
T419	Oak	A	9	
G475	Ash, willow	U		Fell for management
T476	Ash	C	3.6	
T477	Oak	A	13.2	
T478	Ash	C	3.6	
H479	Blackthorn	C	1.2	
T480	Ash	U		
G481	Oak, ash, willow, field maple	B	7.2	
T482	Ash	U		
T483	Oak	B	10.8	
T484	Oak	B	9.6	
T485	Ash	C	9	
T486	Ash	C	4.2	
T487	Ash	C	3.9	
H488	Hawthorn	C	1.8	Fell for development

SGN 1 *Monitoring tree protection*

Always:
- ✓ have a pre-commencement meeting with the tree consultant before development starts
- ✓ use the tree consultant to regularly check that protection remains fit for purpose
- ✓ use the tree consultant to supervise work in RPAs
- ✓ keep a written record of supervision

SGN 2 *Fencing protected trees*

Always:
- ✓ install protection before development starts
- ✓ make sure protection is fit for purpose, i.e. it prevents damage to trees and soil
- ✓ keep protection in place until there is no risk to trees
- ✓ get written permission to move or remove any protection

SGN 4 *Pollution control*

Always:
- ✓ keep toxic products away from RPAs

SGN 11 *Installing services in RPAs*

Always:
- ✓ use the tree consultant to supervise work in RPAs
- ✓ select the least damaging option when installing services, so prioritise trenchless, over broken trench over continuous trench
- ✓ hand-dig trenches if trenchless is not feasible

SGN 12 *Landscaping in RPAs*

Always:
- ✓ use the tree consultant to supervise work in RPAs
- ✓ avoid raising ground levels within 1m of the trunks of retained trees

How to use plan

More detailed guidance on each Site Guidance Note (SGN) can be found in a printed hard copy compilation of all the SGNs, **Manual for Managing Trees On Development Sites version 3.1**, issued to the Site Manager at the pre-commencement site meeting (**Note:** This should be retained on site throughout the duration of works). Additionally, an electronic pdf compilation of all the SGNs, was submitted with this drawing to the local planning authority and the client. Alternatively, a pdf of each SGN can be downloaded by:

1. clicking the image links in the electronic pdf version of this plan;
2. holding a mobile phone QR (Quick Response) code reader over the QR code in the paper version of this plan; or,
3. visiting our website at *https://www.barrelltreecare.co.uk/resources/technical-guidance*
